Crowe's Nest Build

450 SR 27, Whitwell, TN 37397

Construction Started: 2026-04-07

Total Budget: $450,000

1. Budget Summary

Total Budget : $450,000

Amount Spent : $0

Remaining Budget : $450,000

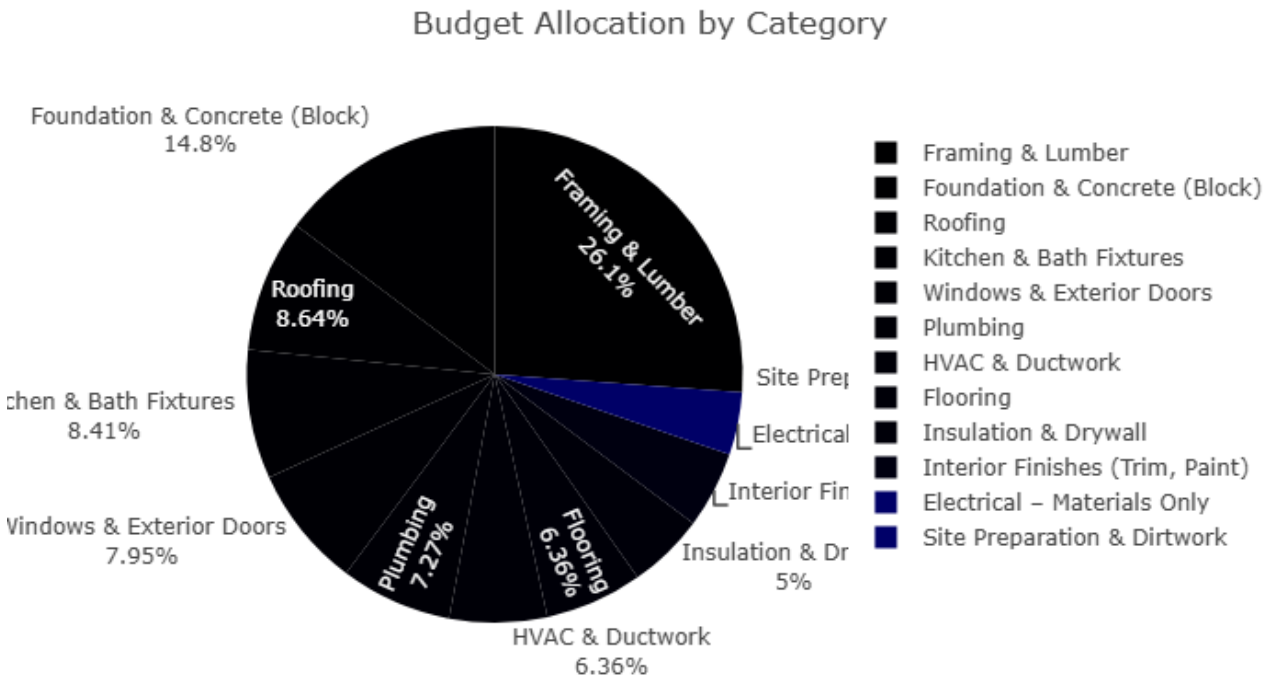

2. Project Gantt

Crowe's Nest Build - Construction Binder

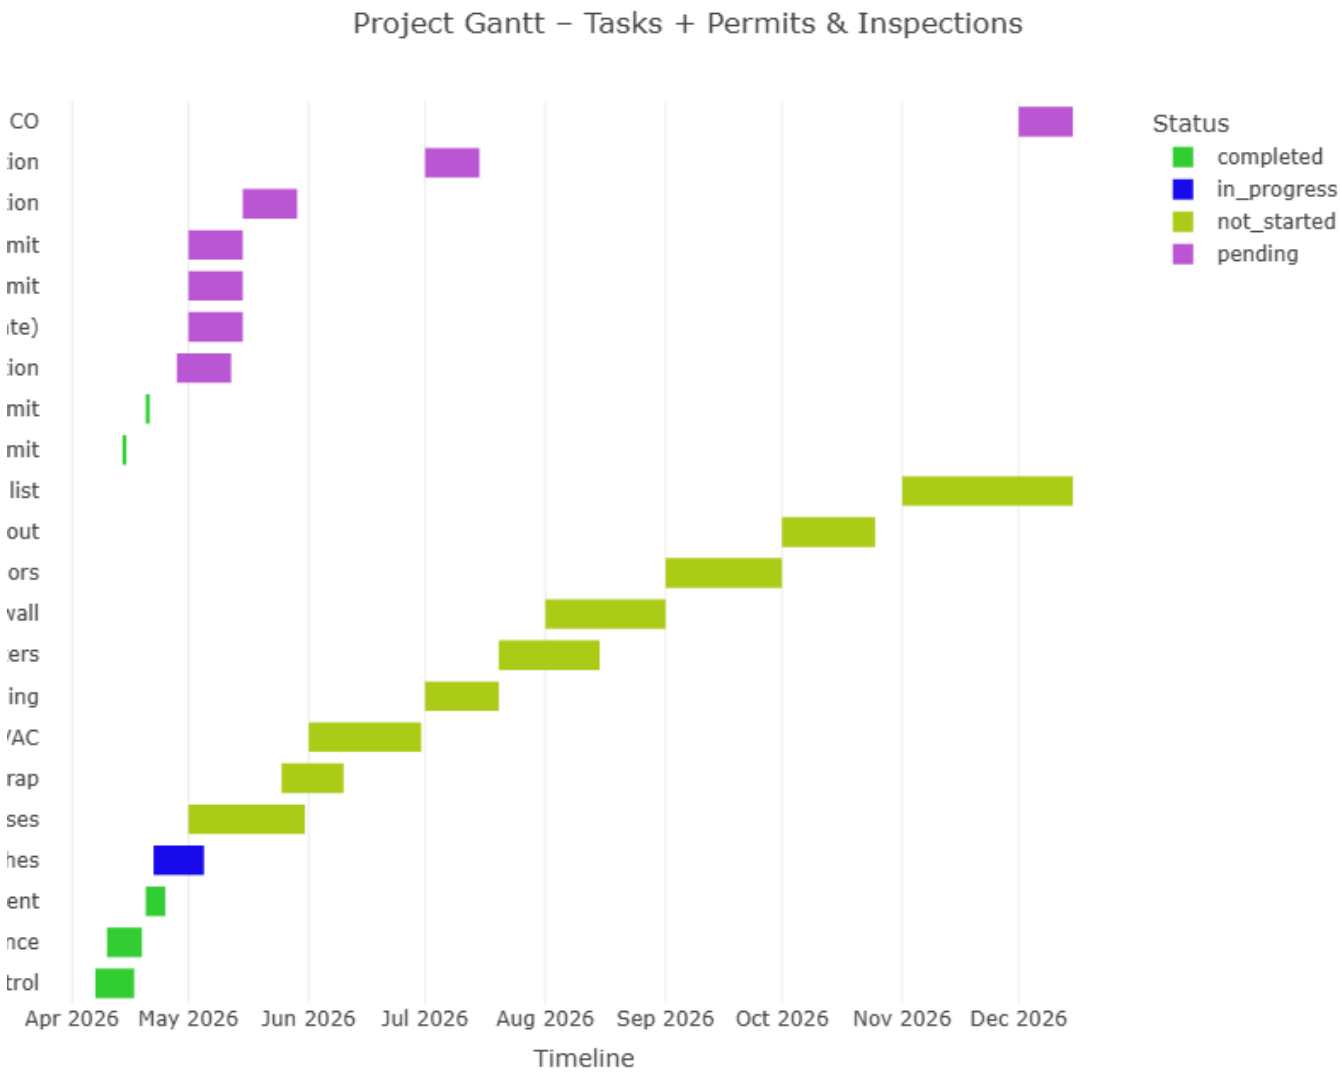

3. Task Progress by Phase

1. Site Preparation: 2/4 tasks complete (50%)
2. Foundation: 1/4 tasks complete (25%)
3. Framing: 0/4 tasks complete (0%)
4. Rough-ins: 0/3 tasks complete (0%)
5. Roofing: 0/3 tasks complete (0%)
6. Exterior Finishes: 0/3 tasks complete (0%)
7. Insulation & Drywall: 0/3 tasks complete (0%)
8. Interior Finishes: 0/3 tasks complete (0%)
9. Fixtures & Appliances: 0/3 tasks complete (0%)
10. Landscaping & Punch List: 0/3 tasks complete (0%)

Crowe's Nest Build - Construction Binder

4. Key Progress Photos

2026-04-24 - newplot.png

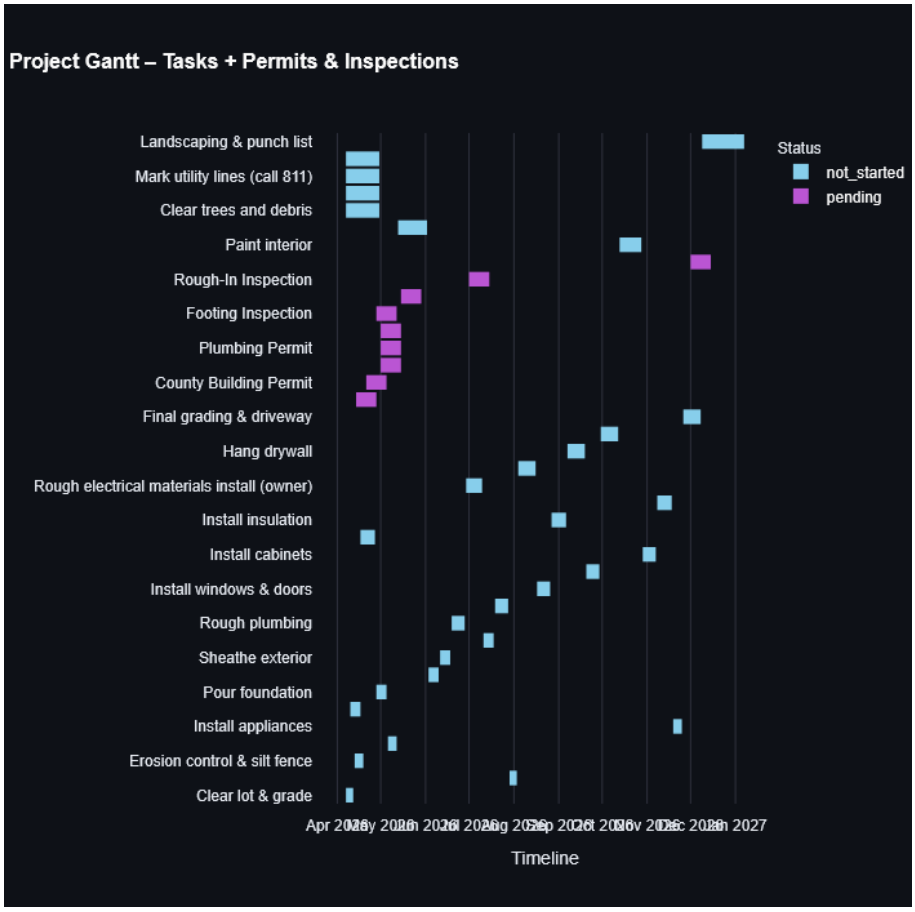

2026-04-24 - image001.png



5. Permits & Inspections

- Septic System Permit - APPROVED (2026-04-14)
- County Building Permit - APPROVED (2026-04-21)
- Footing Inspection - PENDING (2026-04-28)

Crowe's Nest Build - Construction Binder

- Electrical Permit (State) - PENDING (2026-05-01)
- Plumbing Permit - PENDING (2026-05-01)
- Mechanical/HVAC Permit - PENDING (2026-05-01)
- Foundation Inspection - PENDING (2026-05-15)
- Rough-In Inspection - PENDING (2026-07-01)
- Final Inspection & CO - PENDING (2026-12-01)

This document was automatically generated by Crowe's Nest Build
